


CHANGE MANAGEMENT


Step	Time Line	Pro-cedure	En-titled	Sketch	Cause	Result	Actions	Effect (Time, Cost)
------	-----------	------------	-----------	--------	-------	--------	---------	---------------------

SAMPLE: substantiate Cause-Effect-Relations
constitute exhaustive Evidences


1. up to Documents

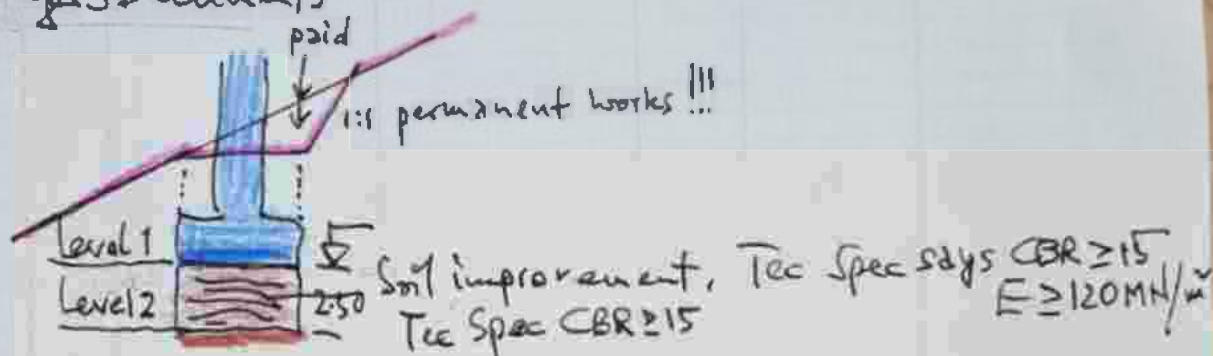

2. Contractor Commence Excavation

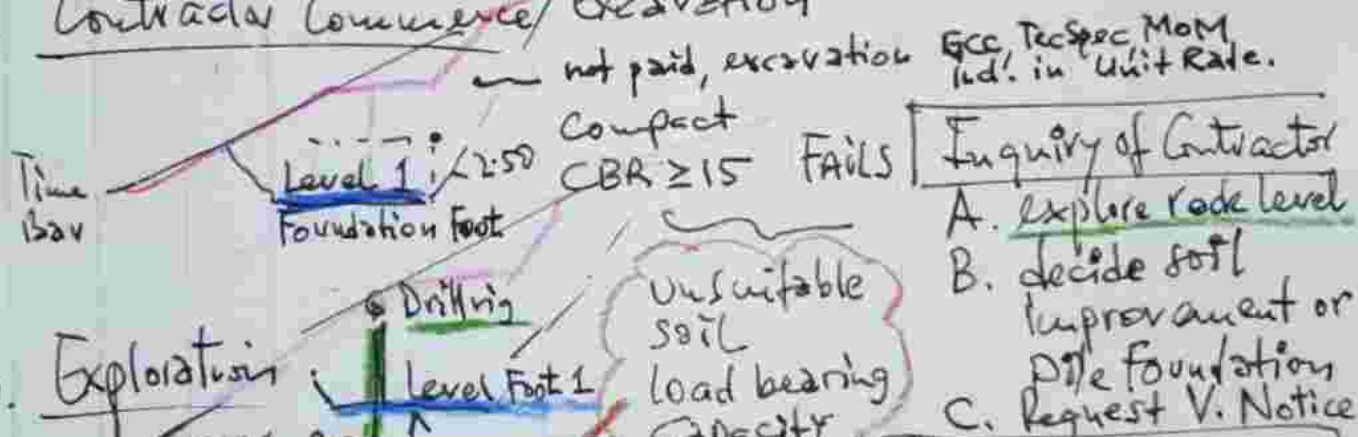


3. Exploration

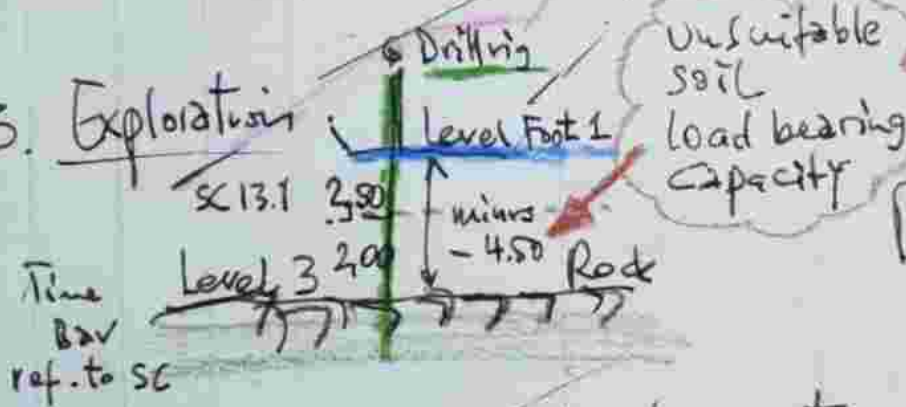

Instruction Engineer
Replace soil - 2.50
Test Compaction, fails
Replace soil - 4.50
up to Rock level
Testing ... Result F/P.

4. Excavation up to soil replacement according drawing.



Instruction to Rock level.

5. Excavation up to Rock level - Soil improvement by replacement

Timebar SC B.1

© HFG2404

Change Management! Circumstantiate Cause-Effect: → Evidences

Step	Time Line	Pro-cedure	En-titled	Sketch	Cause	Result	Actions	Effect (Time, Cost)
------	-----------	------------	-----------	--------	-------	--------	---------	---------------------

5. Soil improvement to Rocklevel

6. ~~paid 512.1~~ ~~paid 512.1~~ ~~paid 512.1~~ ~~???~~ ~~???~~ ~~???~~ ~~Tec Spec / MoM inconsistent~~

6a. compact CBR > 15, passes

6b. crushed aggregates to replace unsuitable soil in Layers (250 mm) plus

6c. lean concrete/blinding level layer 0.15m C12/C15 XCO

As-built Drawing to certify

7. Justification

The Contractor had followed the Instruction given by Engineer

The Instruction was based on the failed Requirement acc to Tec Spec item ???

The Contractor shall provide a Variation Note to record the Quantity increase. No new rate/new price is required. As-built Drawg to sub...

1. Soil improvement level 1 - level 3 Excavation 4.50 m
2. Crushed aggregate layers 4.35 m
3. lean Concrete layer C12/C15 Level Course 0.15 m thick

509.1
B.O.Q
509.2

Note: The disruption time may cause later EoT/FC if not on critical path.....

Cost = + [LC, FC, Euro] Disruption + 4 day + 0 days.

↳ Notice of Determination (NOD) HEGZM
↳ IPA/IPC/Contract Price.
